



City of South Fulton Department of Public Works  
**T271 Fairburn Road Upgrade, Phase II**  
**Upgrade**

Council District(s): 1

ARC No.

PI

Project Manager:


**PROJECT SCOPE:**

The project is located on Fairburn Road, starting at the Fairburn Road/Utoy Springs Road connector to North Utoy Creek. The typical section includes curb and gutter, 2-foot stamped concrete, a 10-foot multi-use path on the West side and a 6-foot wide sidewalk on the east side of Fairburn Road. Improvements also include bridge replacements at North and South Utoy Creek with a bottomless culvert and turning lane improvements at the Fairburn Road/Cascade Road intersection. Project is approximately 0.42 mile.

**R.O.W. DATA:** Total Parcels 8 Acquired 6 Remaining 2 Certified:

**PROJECT SCHEDULE:**

**DESIGN:** FINAL  
**RIGHT-OF-WAY:** UNDERWAY  
**UTILITIES:** SPRING 2021  
**CONSTRUCTION:** SPRING 2021

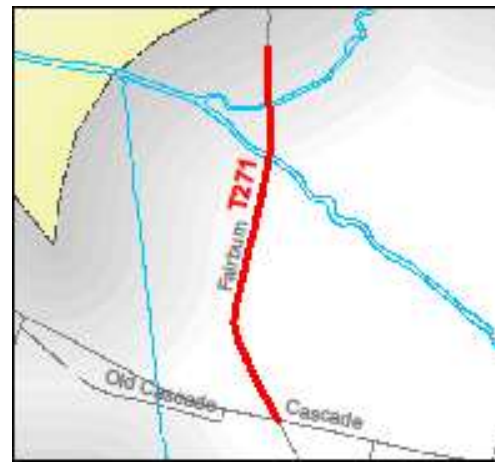

**BUDGET:**

Phase	FY	Funds			Project Costs			Budgeted		
		Federal	State/City	CoSF	Estimated	Type	Amount	FY	Amount	FY
Design:	2016	\$0	\$0	\$199,568	\$199,568	Final	\$0	2020	\$0	2021
ROW:	2017	\$0	\$0	\$51,828	\$51,828	Final	\$0	2020	\$0	2021
Utilities:	2021	\$0	\$0	\$185,830	\$185,830	Final	\$0	2020	\$0	2021
Construction:	2021	\$0	\$0	\$2,980,121	\$2,980,121	Final	\$736,028	2020	\$2,941,111	2021
Total:		\$0	\$0	\$3,417,347	\$3,417,347		\$736,028		\$2,941,111	

**COMPLETED ITEMS:** Design will be completed upon right-of-way (ROW) acquisition

**PENDING ITEMS:** ROW acquisition (5 of 8 parcels acquired)

**ACTION ITEMS:** Consultant to resume design activities. Consultant to resume right-of-way acquisition
