



**City of South Fulton Department of Public Works
T265 Old National Sidewalks, Flat Shoals to Jonesboro Road (Phase II)
Sidewalks**

Council District(s): 6

ARC No. FS-288

PI 0010730/0015

Project Manager:


PROJECT SCOPE:

The project consists of a transit-oriented streetscape along both sides of Old National Highway (S.R. 279) beginning at Flat Shoals Road and continues to Jonesboro Road. Design of sidewalk system consists of 2-foot wide stamped concrete installed at the back of the existing curb, a 5 to 6 foot-wide sidewalks on both sides of Old National Highway, landscaping, and signal upgrades. Signal upgrades will be completed at the intersections along Old National Highway and (Bethsaida Road/Creel Road/Woodward Road/McGhee Landing and Flat Shoals Road). The project length is 2.6 miles.

R.O.W. DATA: Total Parcels 28 Acquired 0 Remaining 28 Certified:

PROJECT SCHEDULE:

DESIGN: PRELIMINARY
RIGHT-OF-WAY: SPRING 2020
UTILITIES: SPRING 2021
CONSTRUCTION: SPRING 2021

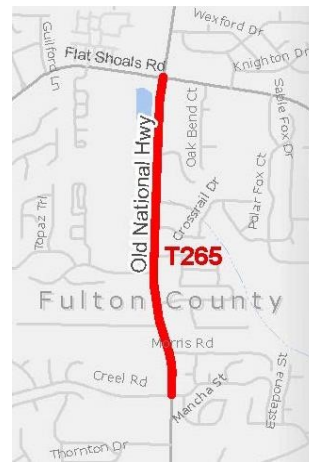

BUDGET:

Phase	FY	Funds			Project Costs			Budgeted		
		Federal	State/City	CoSF	Estimated	Type	Amount	FY	Amount	FY
Design:	2020	\$0	\$0	\$261,872	\$261,872	Final	\$0	2020	\$0	2021
ROW:	2020	\$300,000	\$0	\$748,000	\$1,048,000	Preliminary	\$79,153	2020	\$187,198	2021
Utilities:	2021	\$160,000	\$0	\$50,000	\$210,000	Preliminary	\$0	2020	\$0	2021
Construction:	2021	<u>\$2,838,000</u>	<u>\$0</u>	<u>\$1,036,826</u>	<u>\$3,874,826</u>	Preliminary	<u>\$0</u>	2020	<u>\$0</u>	2021
Total:		\$3,298,000	\$0	\$2,096,698	\$5,394,698		\$79,153		\$187,198	

COMPLETED ITEMS: ROW plans submitted to GDOT.

PENDING ITEMS: Purchase order to consultant (QK4) to resume design activities

ACTION ITEMS: Notice to proceed to commence right-of-way acquisition
