



**City of South Fulton Department of Public Works**  
**T270 Demooney Road over Deep Creek**  
**Bridge Replacement**

**Council District(s): 4**

**ARC No.** FS-286A

**PI** 0015083

**Project Manager:**


**PROJECT SCOPE:**

The proposed project will replace the bridge carrying Demooney Road over Deep Creek. The project begins 1,000 ft. southwest of the existing bridge and ends 980 ft. northeast of the existing bridge. This project would replace the existing substandard bridge over Deep Creek with a new structure and new roadway approaches. The proposed mainline will consist of two 12'-0" travel lanes and curb and gutter in each direction. Sidewalks will be constructed in each direction for the full project length. A 2.0' buffer will be provided between the sidewalk and curb.

**R.O.W. DATA:** Total Parcels 6 Acquired 0 Remaining 6 Certified:

**PROJECT SCHEDULE:**

**DESIGN:** PRELIMINARY  
**RIGHT-OF-WAY:** TBD  
**UTILITIES:** TBD  
**CONSTRUCTION:** TBD

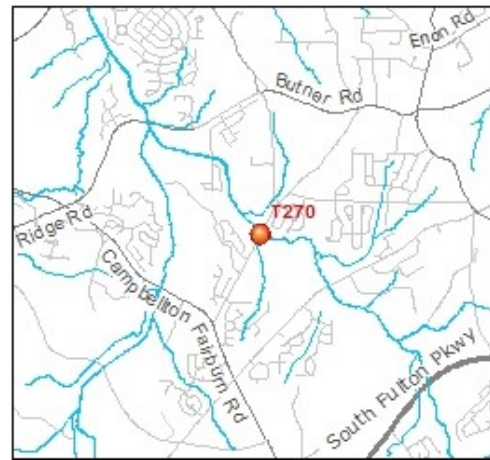

**BUDGET:**

Phase	FY	Funds			Project Costs			Budgeted		
		Federal	State/City	CoSF	Estimated	Type	Amount	FY	Amount	FY
Design:	2016	\$240,000	\$0	\$59,687	\$299,687	Final	\$30,383	2020	\$10,128	2021
ROW:		\$0	\$0	\$80,000	\$80,000	Conceptual	\$38,146	2020	\$63,743	2021
Utilities:		\$0	\$0	\$40,000	\$40,000	Conceptual	\$0	2020	\$0	2021
Construction:		\$0	\$0	\$1,800,000	\$1,800,000	Conceptual	\$0	2020	\$0	2021
<b>Total:</b>		\$240,000	\$0	\$1,979,687	\$2,219,687		\$68,529		\$73,871	

**COMPLETED ITEMS:** Concept approved. PIOH held on July 17, 2018. Comments received on Hydraulic and Hydrology report with preliminary bridge layout.

**PENDING ITEMS:** Approval of federal funds

**ACTION ITEMS:** Consultant to resume design activities
