



City of South Fulton Department of Public Works
T277 Cochran Road over Camp Creek
Bridge Replacement

Council District(s): 2

ARC No. FS-286C

PI 0015530

Project Manager:


PROJECT SCOPE:

The proposed project will replace the bridge carrying Cochran Road over Camp Creek. The project begins 220 ft. southwest of the existing bridge and ends 200 ft. northeast of the existing bridge. This project would replace the existing substandard bridge over Camp Creek with a new structure and new roadway approaches. The proposed mainline will consist of two 11'-0" travel lanes and curb and gutter in each direction on the bridge. Sidewalks will be constructed in each direction along the bridge. A 2.0' buffer will be provided between the sidewalk and curb and will be constructed as stamped concrete

R.O.W. DATA: Total Parcels 4 Acquired 0 Remaining 4 Certified:

PROJECT SCHEDULE:

DESIGN: PRELIMINARY
RIGHT-OF-WAY: TBD
UTILITIES: TBD
CONSTRUCTION: TBD

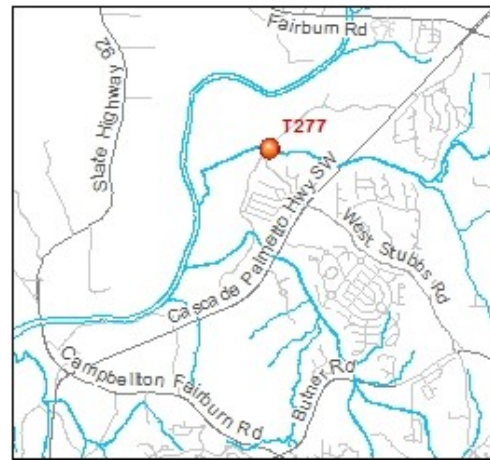

BUDGET:

Phase	FY	Funds			Project Costs			Budgeted		
		Federal	State/City	CoSF	Estimated	Type	Amount	FY	Amount	FY
Design:	2016	\$240,000	\$0	\$59,687	\$299,687	Final	\$0	2020	\$0	2021
ROW:		\$0	\$0	\$50,000	\$50,000	Conceptual	\$38,146	2020	\$63,743	2021
Utilities:		\$0	\$0	\$100,000	\$100,000	Conceptual	\$0	2020	\$0	2021
Construction:		\$0	\$0	\$1,800,000	\$1,800,000	Conceptual	\$0	2020	\$0	2021
Total:		\$240,000	\$0	\$2,009,687	\$2,249,687		\$38,146		\$63,743	

COMPLETED ITEMS: Concept approved. PIOH held on July 16, 2018. Comments received on Hydraulic and Hydrology report with preliminary bridge layout.

PENDING ITEMS: Approval of federal funds

ACTION ITEMS: Consultant to resume design activities
